



Sample Business Project Plan

Sample Conversion to MS Teams Voice

Project Description

Sample Corporate Office is currently utilizing Cisco Unified Communications for Voice Services. The purpose of this project plan is to outline how Sample Implementation Company will transition Sample Corporate office from CUCM to MS Teams Voice Services.

Project Scope

- Sample Corporate office to migrate to MS Teams Voice in Phase 1
- Sample Implementation Company to streamline Voice Services to allow for a more modern technology-driving experience for our business users
- Deploy MS Teams Voice Services to Sample Branches in Phase 2

Objectives

- This document will offer guidance to deliver a standardized method for deploying MS Teams Voice across the Sample Organization within a phased approach.
 - Technical objectives
 - To deliver a robust strategy regarding transitioning our Sample business users to MS Teams Voice. The goal is to decommission Sample's Call Manager and ensure all services are operable such as e911 services to Sample Corporate office and all Sample Branches.
 - To test Voice Services via a Pilot approach with our Sample Business Users within the Sample Network

Deliverables

- Voice Services via MS Teams Voice to Corporate Office phase 1
 - No Auto-Attendant or Call Queue.
 - Port Existing phone numbers over to intelepeer
 - Configure each Sample business user via Intelepeer and Teams Tenant with phone number and e911 Services
- Voice Services via MS Teams Voice to Sample Branches – 29 Sites – Phase 2
 - Deploy MS Voice to 2 Branches per Day
 - Create an Auto Attendant/Call Queue for Each Sample Branch to approve member experience
 - Sample to determine if they will keep existing phone numbers
 - Recommendation: Port Branches Main Number to intelepeer – Transition the main number to an Auto Attendant; Port all branch employee phone numbers to intelepeer and assign their existing phone number to their MS Teams Client. - \$\$\$ Savings on purchasing all new numbers.
 - Note*** about 10 numbers have been ordered for Sample Tenant for testing purposes.
 - Sample Auto Attendant for Sample Havana Branch: +1 720 419 3389 – This would be put in place for each Branch resulting in an improved member experience.

Fundamentals – Already Completed in Sample Teams Tenant

MS Teams Pilot Readiness Checklist

Select a period to highlight at right. A legend describing the charting follows

Period Highlight: 1

Plan Duration

Actual Sta

% Complete

Actual (beyond plan)

% Complete (beyond plan)

[illegible]

Direct Routing feature to test	Results summary	Instructions	Notes
Make a PSTN call by dialing a PSTN number	Pass /Fail	Dial an external cell phone # from MS Teams App	Pass. Called Tim Agnew's PSTN
Receive a PSTN call by dialing your PSTN number from an external line (mobile, landline)	Pass /Fail		Pass
Transfer a PSTN call from one Teams user to another	Pass /Fail		
Start a call from a chat in MS Teams App	Pass /Fail	Go to your chat list, and click New chat New chat button to start a new conversation. Type the name or names into the To field at the top of your new chat. Select Video call Video call button or Audio call Calls button to start a call. Up to 20 people can be on the same video call.	Pass
Test Call Forwarding	Pass/ Fail	Set up call forwarding To start forwarding your calls, select Settings and more Select to see more options next to your profile picture at the top of Teams. Then select Settings > Calls. Under Call answering rules, choose Forward my calls, and then select where you want your forwarded calls to go: voicemail, another person, or a call group. Call answering and forwarding rules You can also find these settings (whenever you're in the Calls area) by selecting Don't forward (or Forward to voicemail, etc.) in the lower-left of Teams.	Selected forward to VM. When calling the first time it rang my phone and didn't forward. The second test did not ring out loud but eventually said "user busy". The third time I tried it rang my MS Teams phone again and did not forward to VM
Make a new call and merge it with an existing call	Pass /Fail	While you're on a call with another person (or a group call), you might decide you want to ask someone else a relevant question. You can make another call while you're still on the first call. When the second call connects, you can merge it with your first call. Note: The first call will automatically be put on hold when you make another call. Or you can go to the call controls and select More actions More options button > Hold to take this action before making another call....When the second call connects, go to the call controls and select More Select Settings and more Select to see more options next to your profile picture at the top of Teams and choose General. Under Delegation, select Manage delegates. Teams-settings-delegation Note: If you don't see any options for delegation in your settings, it's likely because you don't have an Enterprise Voice or Business Voice license. Also note that it can take up to 24 hours for changes in licenses to take effect. Click Your delegates and type the person's name in the Add a delegate box. When you add a delegate, you'll see some permissions settings. In addition to enabling your new delegate to make and receive calls on your behalf, you can also let them change your call and delegate settings for you. Select the permissions you want to give them and click Save. Your delegate will receive a notification letting them know about their new status. Your new delegate will now appear in your delegates list, and this list will be a default selection in your call forwarding and simultaneous ring options. Go to Settings > Calls. Under Forward my calls, you'll see My	Once calls are merged it does indicate unknown participants are joining. I am not sure if there is a way to disable that automated message
Test Add a delegate	Pass /Fail		Don't see any options for delegations - Corrected
Test Voicemail	Pass /Fail	Your voicemail is a familiar tool for getting the most out of your calling experience in Teams. To access your voicemail, go to Calls > History and then select Voicemail.	VM setup and accessed
Test E911	Pass/ Fail	From your MS Teams Client, Select the telephone icon (located on the left-hand side) and dial 933. The Bellco-Corporate address should display on your client. You should also get a recording that indicate what number and address you are calling from.	Failed. Screenshot provided


Pilot Testing Results

Test results available upon request. All tests passed except Call-forwarding from MS Teams Client and e911 works partially

Roadblocks and Corrective Actions

- Call Forwarding is inoperable from Sample MS Teams Client
 - Intelepeer Recommends Sample Business users to forward calls via a portal
 - Reached out to Kathy from zling to schedule a meeting with Sample Implementation Company and Intelepeer for them to resolve issue prior to go-live
- E911 – Works Partially
 - When dialing 933 test line for emergency services, it does state the phone number and location, however there is an error message that indicated location does not have a sufficient Confidence level and if 911 was to be called, it will first be delivered to the national call center for screening and routed to the appropriate public safety route point
 - Will need to get the Network Team involved. Possible issues:
 - Pilot User is not on the subnet list that I placed in MS Teams admin center. Network will need to provide a list of ALL business users subnets. They will need to determine what subnet each user is on and those subnets will need to be added to MS Teams Sample Tenant
 - The Pilot User's Public IP address is not listed in the MS Teams admin Center.
 - Network Team to identify -or- each business user can identify their public IP address: www.whatismyIP.com


Project Team Roles and Responsibilities

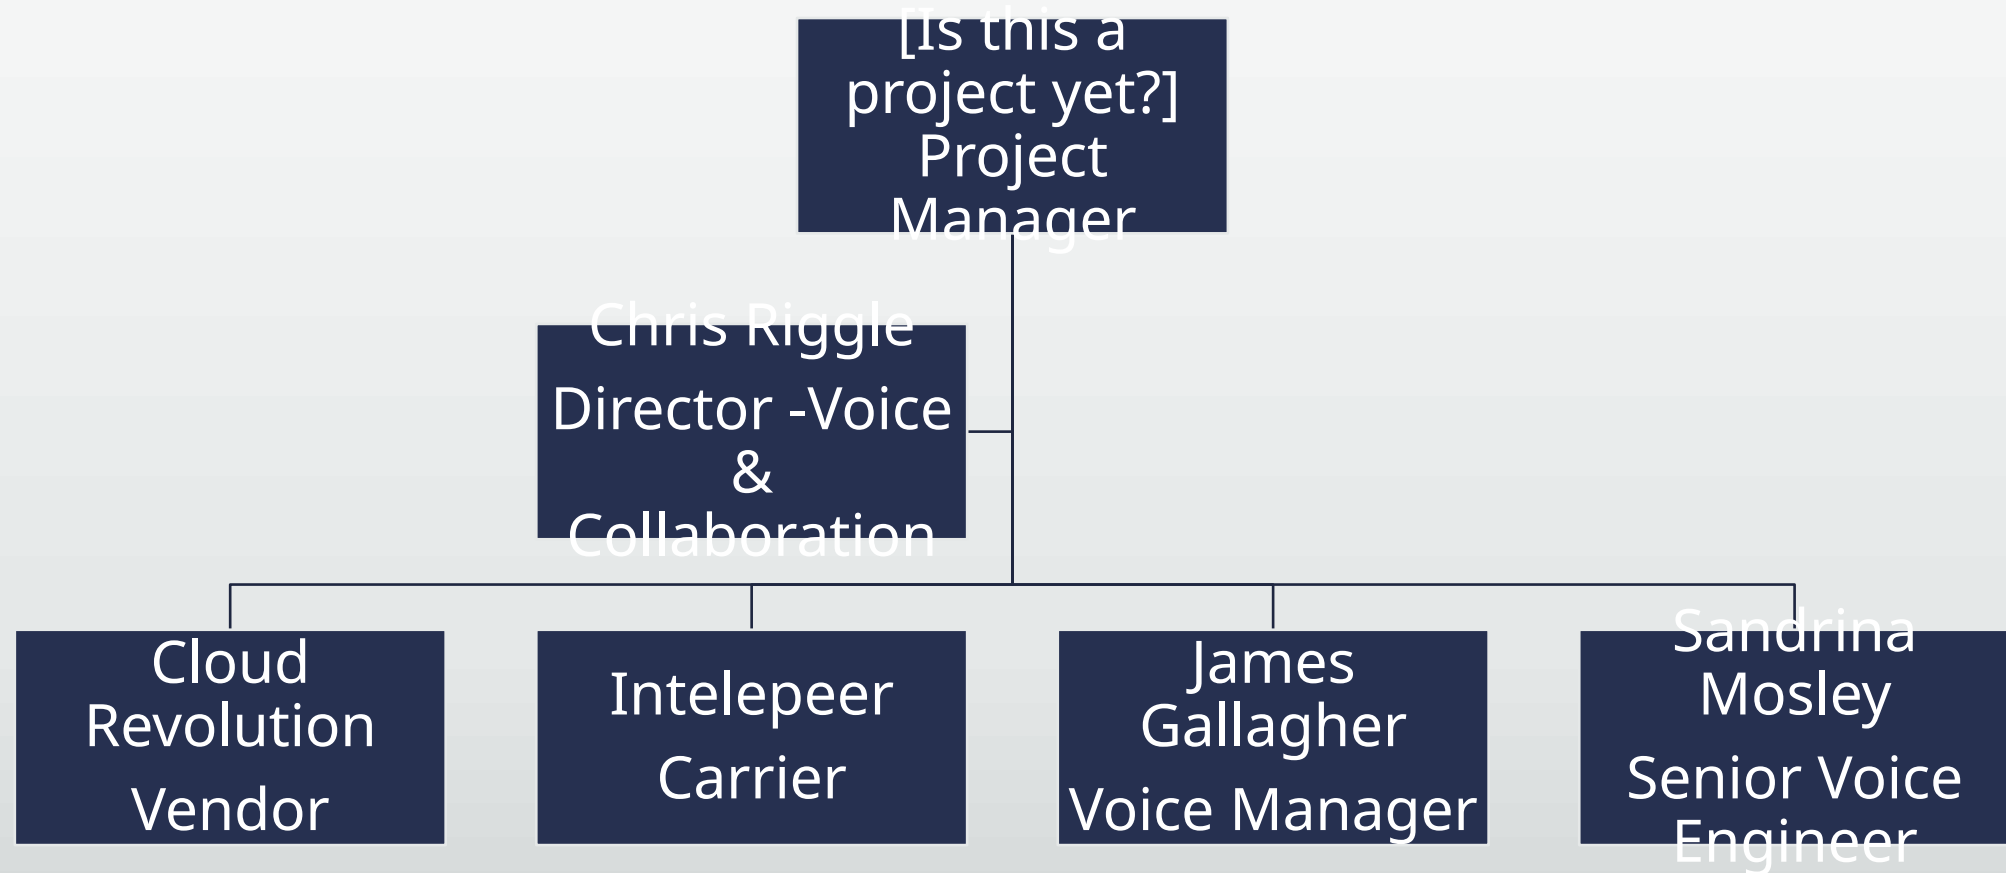

Implementation - Corporate

- Tasks/activities
 - Determine how many Sample Corporate Business users there are
 - Determine phone numbers for each Sample Business User
 - Place Port Request 45 days prior to Go-Live Date
 - Port request will take 30 days
 - With a collaborative approach with the Team, End users should be configured on day 30
- Tools/technology
 - Determine phone number assignments via cucm
 - Create Users via Sample Teams Tenant/Intelepeer
- Project change control process
 - See internal Sample Implementation Company process – This will need to be utilized for porting

Resources

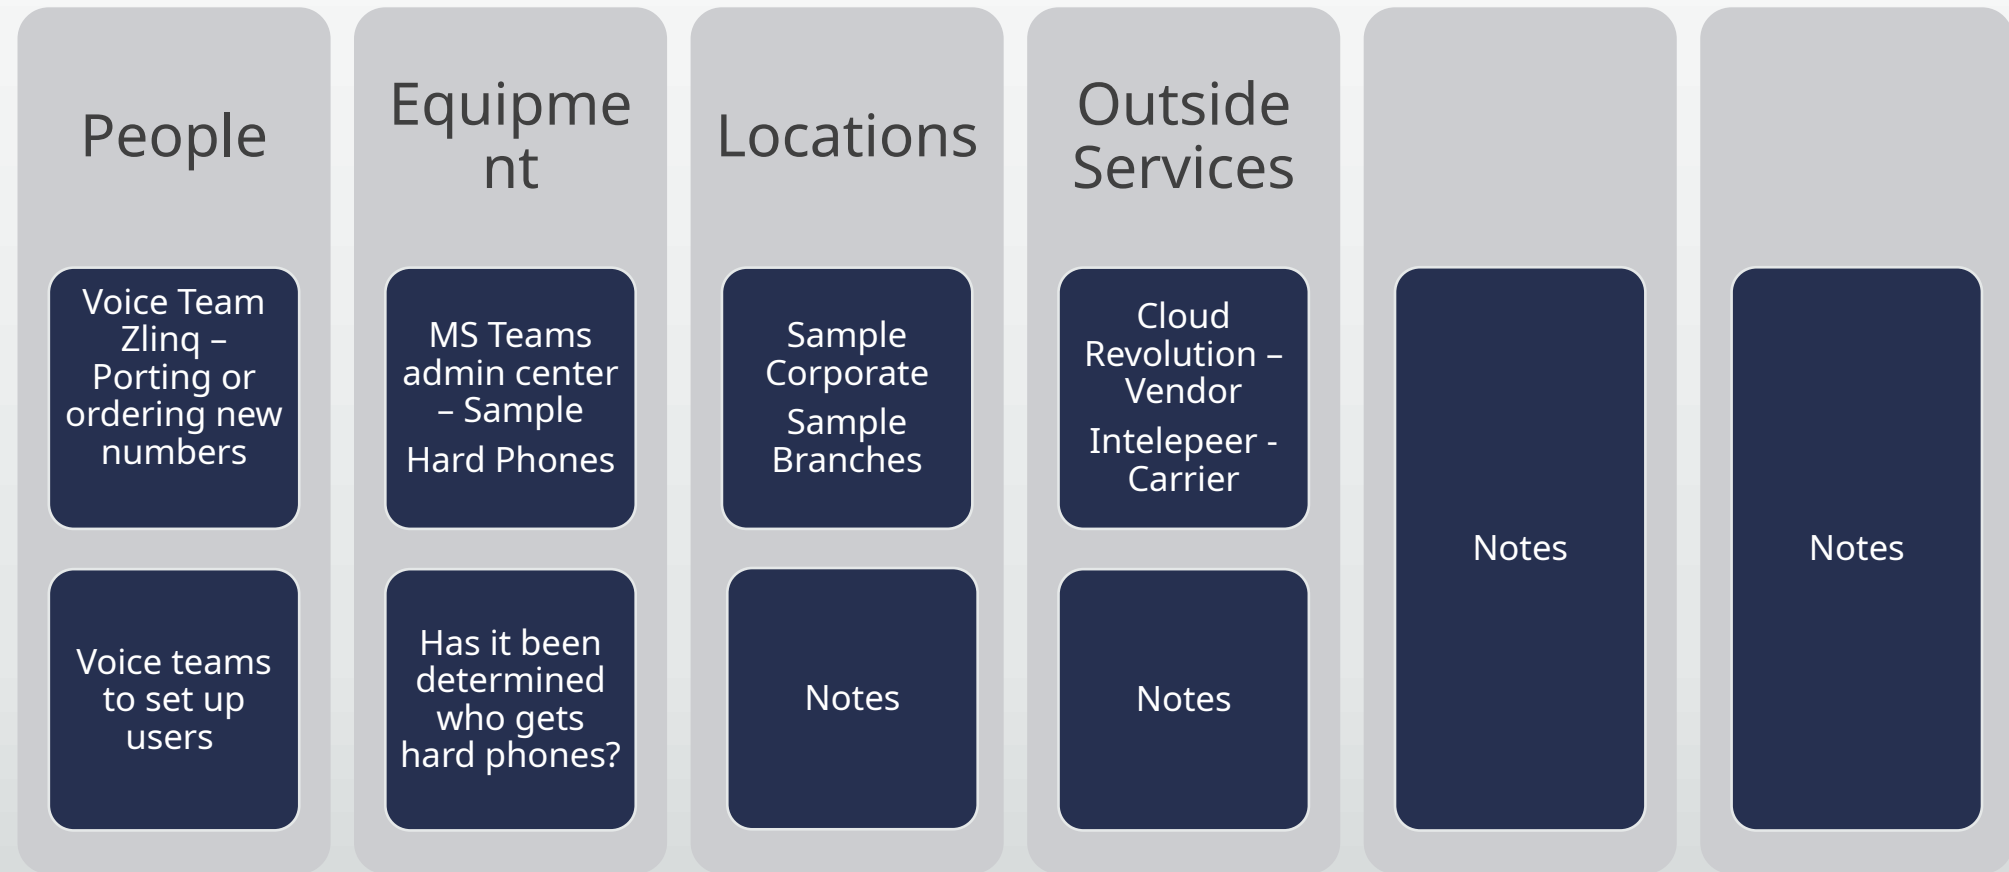

Project Schedule and Milestones



Risk Management Plan

Risk	Probability	Impact	Owner	Mitigation Plan
Porting may affect project scope or schedule.	Medium	High	Project Manager	See appendix for a phased implementation plan
